

**PCS WIRELESS**

# Customer Portal Project Plan

Stage 1 Delivery — 5 Sprints · May to July 2026

DOCUMENT VERSION

**1.0**

DATE

**May 7, 2026**

STATUS

**Draft — Pending Sign-Off**

PREPARED BY

**Development Team**

**5 Sprints — May to July 2026**


# PCS Wireless Customer Portal — Project Plan

**Document Version:** 1.0 **Date:** May 7, 2026 **Stage:** Stage 1 — Core Functionality **Status:** Draft — Pending Business Sign-Off **Prepared by:** Development Team **Review Required From:** Business Stakeholders

## Purpose

This document outlines the delivery plan for Stage 1 of the PCS Wireless Customer Portal. It covers the five-sprint schedule, milestone dates, and the scope delivered in each sprint. The dashboard is built progressively — each sprint adds its corresponding KPI section to the Dashboard page as the feature area it represents goes live.

## Delivery Timeline

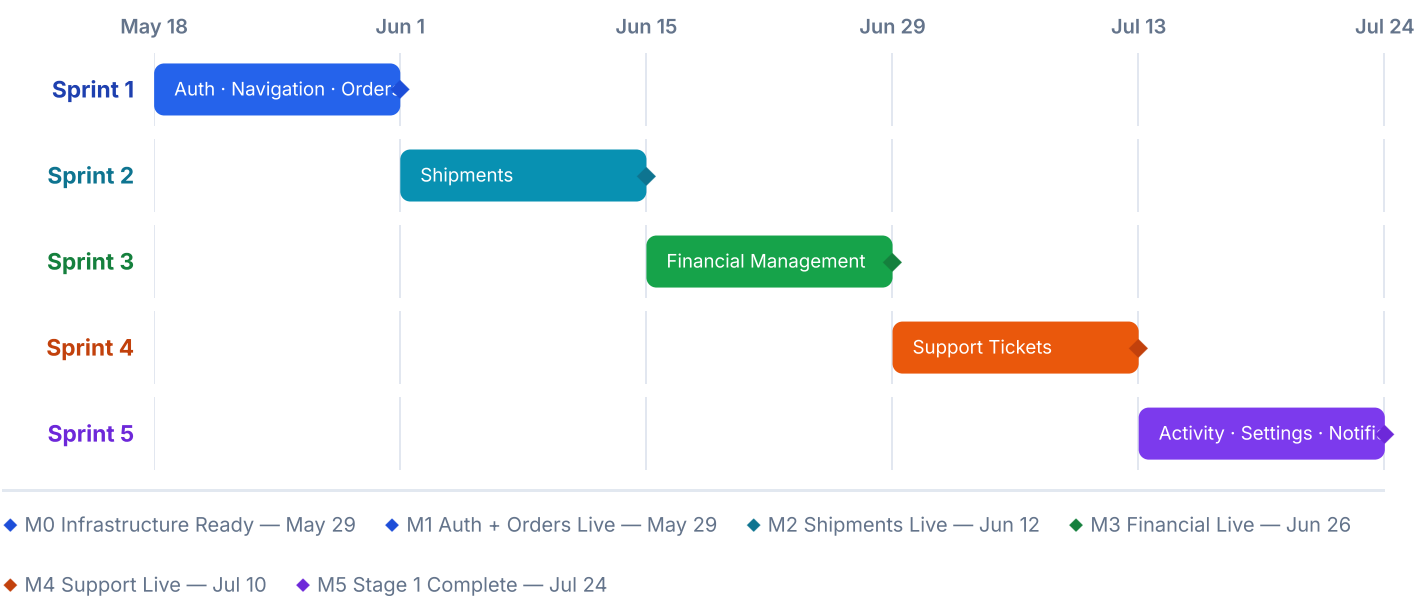

## Milestones

| ID | Milestone                                 | Date         |
|----|-------------------------------------------|--------------|
| M0 | Deploy pipelines and infrastructure ready | May 29, 2026 |

| ID | Milestone                                                                 | Date         |
|----|---------------------------------------------------------------------------|--------------|
| M1 | Authentication and Order Management live — portal accessible to customers | May 29, 2026 |
| M2 | Shipment Tracking live                                                    | Jun 12, 2026 |
| M3 | Financial Management live                                                 | Jun 26, 2026 |
| M4 | Customer Support live                                                     | Jul 10, 2026 |
| M5 | Stage 1 complete — all features live                                      | Jul 24, 2026 |

## Table of Contents

1. [Sprint 1 — Infrastructure, Authentication & Orders](#)
2. [Sprint 2 — Shipments](#)
3. [Sprint 3 — Financial Management](#)
4. [Sprint 4 — Support Tickets](#)
5. [Sprint 5 — Activity Log, Account Settings & Notifications](#)

## 1. Sprint 1 — Infrastructure, Authentication & Orders

**Dates:** May 18 – May 29, 2026 **Milestones:** M0 (May 29) — Infrastructure ready · M1 (May 29) — Portal accessible

### Infrastructure & Deploy Pipelines

| Task                   | Description                                                                  |
|------------------------|------------------------------------------------------------------------------|
| CI/CD pipeline         | GitHub Actions workflow deploying to Render on merge to main                 |
| Staging environment    | Dedicated staging instance on Render for QA before production releases       |
| Production environment | Production web service on Render with environment variable management        |
| PostgreSQL database    | Database provisioned on Render with staging and production instances         |
| Next.js scaffold       | Project initialised with Next.js 14 App Router, Tailwind CSS, and TypeScript |

## Authentication (US-01-04)

| Task                              | User Story                                                       |
|-----------------------------------|------------------------------------------------------------------|
| Auth0 sign-in integration         | US-01 — Customers can log in to the portal                       |
| Password reset flow               | US-02 — Customers can reset a forgotten password                 |
| PCS staff credential provisioning | US-03 — PCS staff provision portal access for existing customers |
| Protected route middleware        | US-04 — All pages require authentication                         |

## Navigation & Global UI (US-67, US-68, US-70)

| Task                                       | User Story                                           |
|--------------------------------------------|------------------------------------------------------|
| Desktop sidebar navigation                 | US-67 — Persistent sidebar with all navigation links |
| Mobile bottom tab bar and hamburger drawer | US-68 — Mobile-friendly navigation                   |
| Responsive layout                          | US-70 — Portal works on both mobile and desktop      |

## Order Management (US-12-16)

| Task                        | User Story                                                        |
|-----------------------------|-------------------------------------------------------------------|
| Order listing page          | US-12 — View a list of all orders                                 |
| Order status filtering      | US-13 — Filter orders by status                                   |
| Order ID / PO Number search | US-14 — Search orders by ID or PO number                          |
| Order detail page           | US-15 — View full order details including line items and shipping |
| Order status timeline       | US-16 — View order progress through fulfilment steps              |

## Dashboard — Sprint 1 Additions (US-06)

| Addition             | Description                      |
|----------------------|----------------------------------|
| Dashboard shell      | Main landing page after login    |
| Open Orders KPI card | Count of orders in active status |

## 2. Sprint 2 — Shipments

**Dates:** Jun 1 – Jun 12, 2026 **Milestone:** M2 (Jun 12) — Shipment Tracking live

## Shipment Tracking (US-20–24)

| Task                       | User Story                                                       |
|----------------------------|------------------------------------------------------------------|
| Shipment listing page      | US-20 — View all shipments associated with the account           |
| Status filter              | US-21 — Filter by In Transit, Delivered, Pickup Ready, Exception |
| Shipment status view       | US-22 — View current status of a shipment                        |
| Last status update display | US-23 — View the most recent status update                       |
| Shipment document download | US-24 — Download Bill of Lading and Packing List                 |

## Dashboard — Sprint 2 Additions

| Addition                   | Description                             |
|----------------------------|-----------------------------------------|
| Pending Shipments KPI card | Count of shipments currently in transit |

## 3. Sprint 3 — Financial Management

**Dates:** Jun 15 – Jun 26, 2026 **Milestone:** M3 (Jun 26) — Financial Management live

### Financial Management (US-30–38)

| Task                        | User Story                                                                   |
|-----------------------------|------------------------------------------------------------------------------|
| Financial summary page      | US-30 — View account financial position                                      |
| Aging breakdown             | US-31 — View outstanding balance by aging bucket (Current, 30, 60, 90+ days) |
| Invoice list and filter     | US-32 — View all invoices with status (Open, Past Due, Paid)                 |
| Invoice detail view         | US-33 — View full invoice with line items and payment history                |
| Invoice PDF download        | US-34 — Download invoice as PDF                                              |
| Account statement download  | US-35 — Download full account statement                                      |
| Invoice dispute             | US-36 — Flag an invoice for review                                           |
| Payment list and detail     | US-37 — View all payments with method, date, amount, and applied invoices    |
| Credit memo list and detail | US-38 — View credit memos with RMA reference and applied invoice             |

## Dashboard — Sprint 3 Additions

| Addition                      | Description                                                  |
|-------------------------------|--------------------------------------------------------------|
| Outstanding Balance KPI card  | Total of all unpaid invoice balances                         |
| Past Due KPI card             | Balance on invoices past their due date                      |
| Past-due invoice alert banner | Banner with link to Financial page when invoices are overdue |

## 4. Sprint 4 — Support Tickets

**Dates:** Jun 29 – Jul 10, 2026 **Milestone:** M4 (Jul 10) — Customer Support live

### Support Tickets (US-45–55)

| Task                                  | User Story                                                                                       |
|---------------------------------------|--------------------------------------------------------------------------------------------------|
| Create new support ticket             | US-45 — Submit a ticket with category, subject, description, priority, and optional linked order |
| Ticket listing page                   | US-46 — View all open and historical support tickets                                             |
| Status and category filter            | US-47 — Filter tickets by status and category                                                    |
| Ticket detail and conversation thread | US-48 — Read the full conversation thread for a ticket                                           |
| Reply to ticket                       | US-49 — Send a reply to a ticket                                                                 |
| File attachment                       | US-50 — Attach files to a support message                                                        |
| Assigned staff display                | US-51 — See which PCS team member is handling the ticket                                         |
| Linked order display                  | US-52 — See if the ticket is linked to a specific order                                          |
| Ticket priority selection             | US-53 — Set priority to Normal or Urgent when creating a ticket                                  |
| Order / Quote ID linking              | US-54 — Link a ticket to an Order ID or Quote ID                                                 |
| Post-resolution rating                | US-55 — Rate the experience after a ticket is resolved                                           |

## Dashboard — Sprint 4 Additions

| Addition                      | Description                             |
|-------------------------------|-----------------------------------------|
| Open Support Tickets KPI card | Count of tickets not in Resolved status |

| Addition                            | Description                                     |
|-------------------------------------|-------------------------------------------------|
| Contact Support quick-action button | Takes the customer directly to the Support page |

## 5. Sprint 5 — Activity Log, Account Settings & Notifications

**Dates:** Jul 13 – Jul 24, 2026 **Milestone:** M5 (Jul 24) — Stage 1 Complete

### Activity Log (US-40–44)

| Task                     | User Story                                                        |
|--------------------------|-------------------------------------------------------------------|
| Full activity log page   | US-40 — View a chronological log of all account events            |
| Category filter          | US-41 — Filter by Orders, Shipments, Payments, Support            |
| Action-required flagging | US-42 — Activities needing attention are visually flagged         |
| Record linking           | US-43 — Each entry links to the related order, invoice, or ticket |
| Date-grouped display     | US-44 — Activities grouped by date                                |

### Account Settings (US-56–66)

| Task                        | User Story                                                     |
|-----------------------------|----------------------------------------------------------------|
| Company profile editing     | US-56 — Update company name, address, phone, email             |
| Tax certificate upload      | US-57 — Manage tax exemption status and upload certificate     |
| Invite users                | US-58 — Invite new team members to the portal account          |
| Assign user roles           | US-59 — Assign Admin, Buyer, or Viewer roles                   |
| Activate / deactivate users | US-60 — Control who has access to the portal                   |
| Theme preference            | US-61 — Choose Light, Dark, or System theme                    |
| Notification preferences    | US-62 — Control which email and SMS notifications are received |
| Regional settings           | US-63 — Set currency, timezone, and date format                |
| Password change             | US-64 — Change account password                                |
| Two-Factor Authentication   | US-65 — Enable 2FA via Authenticator App or SMS                |
| Active session management   | US-66 — View and revoke active login sessions                  |

## Notifications (US-71-73)

| Task                     | User Story                                                     |
|--------------------------|----------------------------------------------------------------|
| Email notifications      | US-71 — Receive emails for key account events                  |
| SMS notifications        | US-72 — Receive SMS alerts for urgent events                   |
| In-app notification bell | US-73 — View in-app alerts via notification bell in the header |

## Navigation completion (US-69)

| Task                  | User Story                                                                                                |
|-----------------------|-----------------------------------------------------------------------------------------------------------|
| Sales rep info in nav | US-69 — Customer's assigned PCS Sales Representative name, phone, and email shown in the navigation panel |

## Dashboard — Sprint 5 Additions

| Addition                    | Description                                                         |
|-----------------------------|---------------------------------------------------------------------|
| Recent activity feed        | The last several account events shown with links to related records |
| Notification bell in header | Unread count badge; clicking opens the alert panel                  |

*End of Document*
