

PCS WIRELESS

Customer Portal Project Plan

Stage 1 Delivery — 5 Sprints · May to July 2026

DOCUMENT VERSION

1.0

DATE

May 7, 2026

STATUS

Draft — Pending Sign-Off

PREPARED BY

Development Team

5 Sprints — May to July 2026

PCS Wireless Customer Portal — Project Plan

Document Version: 1.0 **Date:** May 7, 2026 **Stage:** Stage 1 — Core Functionality **Status:** Draft — Pending Business Sign-Off **Prepared by:** Development Team **Review Required From:** Business Stakeholders


Purpose


This document outlines the delivery plan for Stage 1 of the PCS Wireless Customer Portal. It covers the five-sprint schedule, milestone dates, and the scope delivered in each sprint. The dashboard is built progressively — each sprint adds its corresponding KPI section to the Dashboard page as the feature area it represents goes live.

Technology Stack

Layer	Technology
Frontend & Backend	Next.js 14 (App Router) with Tailwind CSS
Database	PostgreSQL
Authentication	Auth0 with Microsoft Entra ID
Hosting	Render (Node.js web service)
Source Control	GitHub — thomastorvpcs/pcs-customer-portal

Delivery Timeline

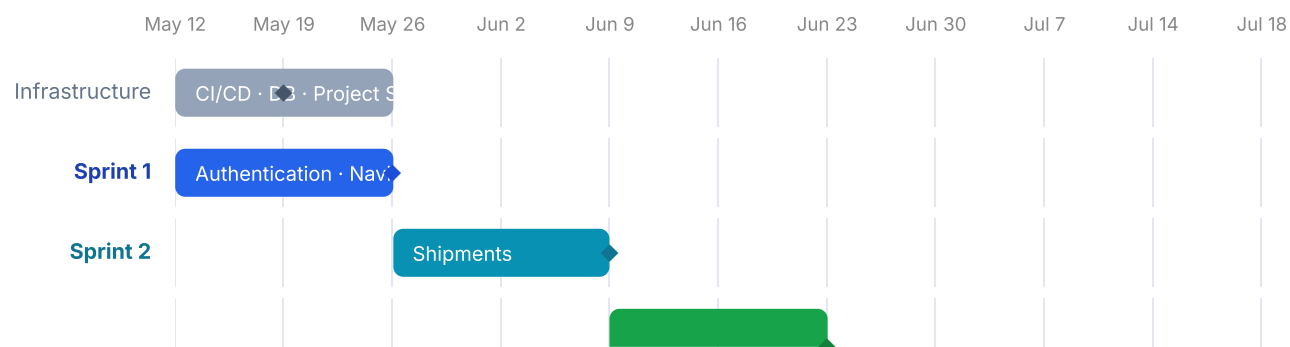

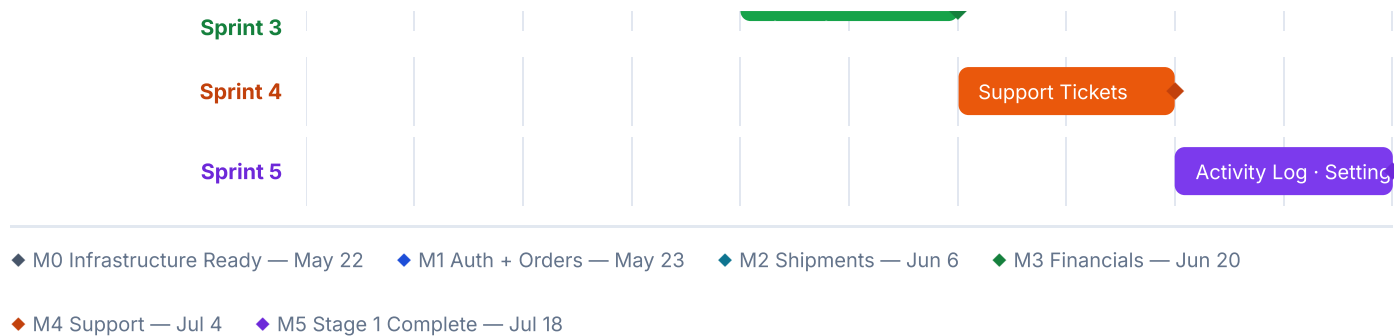

Milestones

ID	Milestone	Date
M0	Deploy pipelines and infrastructure ready	May 22, 2026
M1	Authentication and Order Management live — portal accessible to customers	May 23, 2026
M2	Shipment Tracking live	Jun 6, 2026
M3	Financial Management live	Jun 20, 2026
M4	Customer Support live	Jul 4, 2026
M5	Stage 1 complete — all features live	Jul 18, 2026

Table of Contents

1. [Sprint 1 — Infrastructure, Authentication & Orders](#)
2. [Sprint 2 — Shipments](#)
3. [Sprint 3 — Financial Management](#)
4. [Sprint 4 — Support Tickets](#)
5. [Sprint 5 — Activity Log, Account Settings & Notifications](#)

1. Sprint 1 — Infrastructure, Authentication & Orders

Dates: May 12 – May 23, 2026 **Milestone:** M0 (May 22) — Infrastructure ready · M1 (May 23) — Portal accessible

Infrastructure & Deploy Pipelines

Task	Description
CI/CD pipeline	GitHub Actions workflow deploying to Render on merge to main
Staging environment	Dedicated staging instance on Render for QA before production releases
Production environment	Production web service on Render with environment variable management
PostgreSQL database	Database provisioned on Render with staging and production instances
Next.js scaffold	Project initialised with Next.js 14 App Router, Tailwind CSS, and TypeScript

Authentication (US-01-04)

Task	User Story
Auth0 sign-in integration	US-01 — Customers can log in to the portal
Password reset flow	US-02 — Customers can reset a forgotten password
PCS staff credential provisioning	US-03 — PCS staff provision portal access for existing customers
Protected route middleware	US-04 — All pages require authentication

Navigation & Global UI (US-67, US-68, US-70)

Task	User Story
Desktop sidebar navigation	US-67 — Persistent sidebar with all navigation links
Mobile bottom tab bar and hamburger drawer	US-68 — Mobile-friendly navigation
Responsive layout	US-70 — Portal works on both mobile and desktop

Order Management (US-12-16)

Task	User Story
Order listing page	US-12 — View a list of all orders
Order status filtering	US-13 — Filter orders by status
Order ID / PO Number search	US-14 — Search orders by ID or PO number
Order detail page	US-15 — View full order details including line items and shipping
Order status timeline	US-16 — View order progress through fulfilment steps

Dashboard — Sprint 1 Additions (US-06)

Addition	Description
Dashboard shell	Main landing page after login
Open Orders KPI card	Count of orders in active status

2. Sprint 2 — Shipments

Dates: May 26 – Jun 6, 2026 **Milestone:** M2 (Jun 6) — Shipment Tracking live

Shipment Tracking (US-20–24)

Task	User Story
Shipment listing page	US-20 — View all shipments associated with the account
Status filter	US-21 — Filter by In Transit, Delivered, Pickup Ready, Exception
Shipment status view	US-22 — View current status of a shipment
Last status update display	US-23 — View the most recent status update
Shipment document download	US-24 — Download Bill of Lading and Packing List

Dashboard — Sprint 2 Additions

Addition	Description
Pending Shipments KPI card	Count of shipments currently in transit

3. Sprint 3 — Financial Management

Dates: Jun 9 – Jun 20, 2026 **Milestone:** M3 (Jun 20) — Financial Management live

Financial Management (US-30–38)

Task	User Story
Financial summary page	US-30 — View account financial position
Aging breakdown	US-31 — View outstanding balance by aging bucket (Current, 30, 60, 90+ days)

Task	User Story
Invoice list and filter	US-32 — View all invoices with status (Open, Past Due, Paid)
Invoice detail view	US-33 — View full invoice with line items and payment history
Invoice PDF download	US-34 — Download invoice as PDF
Account statement download	US-35 — Download full account statement
Invoice dispute	US-36 — Flag an invoice for review
Payment list and detail	US-37 — View all payments with method, date, amount, and applied invoices
Credit memo list and detail	US-38 — View credit memos with RMA reference and applied invoice

Dashboard — Sprint 3 Additions

Addition	Description
Outstanding Balance KPI card	Total of all unpaid invoice balances
Past Due KPI card	Balance on invoices past their due date
Past-due invoice alert banner	Banner with link to Financial page when invoices are overdue

4. Sprint 4 — Support Tickets

Dates: Jun 23 – Jul 4, 2026 **Milestone:** M4 (Jul 4) — Customer Support live

Support Tickets (US-45–55)

Task	User Story
Create new support ticket	US-45 — Submit a ticket with category, subject, description, priority, and optional linked order
Ticket listing page	US-46 — View all open and historical support tickets
Status and category filter	US-47 — Filter tickets by status and category
Ticket detail and conversation thread	US-48 — Read the full conversation thread for a ticket
Reply to ticket	US-49 — Send a reply to a ticket
File attachment	US-50 — Attach files to a support message

Task	User Story
Assigned staff display	US-51 — See which PCS team member is handling the ticket
Linked order display	US-52 — See if the ticket is linked to a specific order
Ticket priority selection	US-53 — Set priority to Normal or Urgent when creating a ticket
Order / Quote ID linking	US-54 — Link a ticket to an Order ID or Quote ID
Post-resolution rating	US-55 — Rate the experience after a ticket is resolved

Dashboard — Sprint 4 Additions

Addition	Description
Open Support Tickets KPI card	Count of tickets not in Resolved status
Contact Support quick-action button	Takes the customer directly to the Support page

5. Sprint 5 — Activity Log, Account Settings & Notifications

Dates: Jul 7 – Jul 18, 2026 **Milestone:** M5 (Jul 18) — Stage 1 Complete

Activity Log (US-40–44)

Task	User Story
Full activity log page	US-40 — View a chronological log of all account events
Category filter	US-41 — Filter by Orders, Shipments, Payments, Support
Action-required flagging	US-42 — Activities needing attention are visually flagged
Record linking	US-43 — Each entry links to the related order, invoice, or ticket
Date-grouped display	US-44 — Activities grouped by date

Account Settings (US-56–66)

Task	User Story
Company profile editing	US-56 — Update company name, address, phone, email
Tax certificate upload	US-57 — Manage tax exemption status and upload certificate
Invite users	US-58 — Invite new team members to the portal account

Task	User Story
Assign user roles	US-59 — Assign Admin, Buyer, or Viewer roles
Activate / deactivate users	US-60 — Control who has access to the portal
Theme preference	US-61 — Choose Light, Dark, or System theme
Notification preferences	US-62 — Control which email and SMS notifications are received
Regional settings	US-63 — Set currency, timezone, and date format
Password change	US-64 — Change account password
Two-Factor Authentication	US-65 — Enable 2FA via Authenticator App or SMS
Active session management	US-66 — View and revoke active login sessions

Notifications (US-71-73)

Task	User Story
Email notifications	US-71 — Receive emails for key account events
SMS notifications	US-72 — Receive SMS alerts for urgent events
In-app notification bell	US-73 — View in-app alerts via notification bell in the header

Navigation completion (US-69)

Task	User Story
Sales rep info in nav	US-69 — Customer's assigned PCS Sales Representative name, phone, and email shown in the navigation panel

Dashboard — Sprint 5 Additions

Addition	Description
Recent activity feed	The last several account events shown with links to related records
Notification bell in header	Unread count badge; clicking opens the alert panel

Sign-Off

Reviewer	Role	Decision	Date	Comments
----------	------	----------	------	----------

--

Decision options: Approved / Approved with Changes / Not Approved

End of Document
